MHD FADLY HASAN
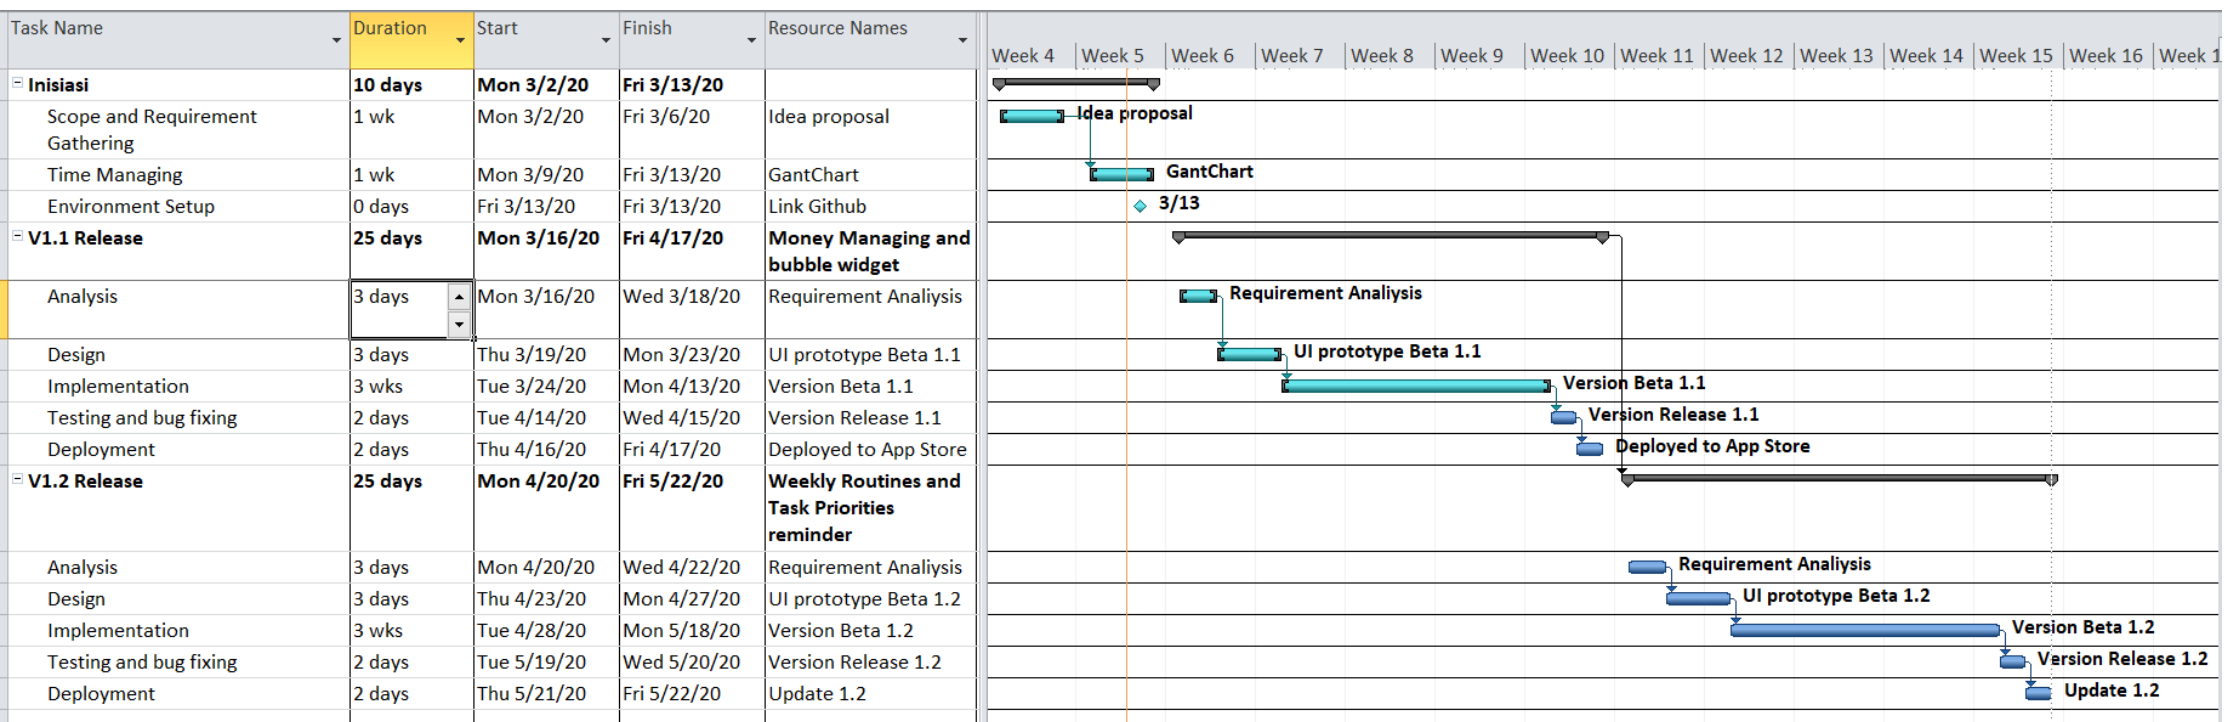## 05111740000078

Gantt Chart

Task Name	Duration	Start	Finish	Resource Names
Inisiasi	10 days	Mon 3/2/20	Fri 3/13/20	
Scope and Requirement Gathering	1 wk	Mon 3/2/20	Fri 3/6/20	Idea proposal
Time Managing	1 wk	Mon 3/9/20	Fri 3/13/20	GantChart
Environment Setup	0 days	Fri 3/13/20	Fri 3/13/20	Link Github
V1.1 Release	25 days	Mon 3/16/20	Fri 4/17/20	Money Managing and bubble widget
Analysis	3 days	Mon 3/16/20	Wed 3/18/20	Requirement Analiysis
Design	3 days	Thu 3/19/20	Mon 3/23/20	UI prototype Beta 1.1
Implementation	3 wks	Tue 3/24/20	Mon 4/13/20	Version Beta 1.1
Testing and bug fixing	2 days	Tue 4/14/20	Wed 4/15/20	Version Release 1.1
Deployment	2 days	Thu 4/16/20	Fri 4/17/20	Deployed to App Store
V1.2 Release	25 days	Mon 4/20/20	Fri 5/22/20	Weekly Routines and Task Priorities reminder
Analysis	3 days	Mon 4/20/20	Wed 4/22/20	Requirement Analiysis
Design	3 days	Thu 4/23/20	Mon 4/27/20	UI prototype Beta 1.2
Implementation	3 wks	Tue 4/28/20	Mon 5/18/20	Version Beta 1.2
Testing and bug fixing	2 days	Tue 5/19/20	Wed 5/20/20	Version Release 1.2
Deployment	2 days	Thu 5/21/20	Fri 5/22/20	Update 1.2

Link Github

https://github.com/mhdfadlyhasan/05111740000078-Andromaid
